

**UPDATE**

May 15, 2019

## Residual Solids Conveyance Line: Pipe Installation

Construction of the Residual Solids Conveyance Line is making good progress with over 30% of the pipes installed. The contractor, Don Mann Excavating, has multiple crews working along the 19km alignment. The updated progress map and work locations are shown on the next page; please visit [wastewaterproject.ca](http://wastewaterproject.ca) for weekly updates.

### What to Expect

- The pipe will be installed in segments.
- A trench will be excavated, the pipes will be installed and the trench will be backfilled. The surface will be temporarily restored at the end of each work day.
- Final restoration will take place after each section has been tested and completed.
- Rock encountered in the trench will be removed by blasting or mechanical means.
- Noise associated with this work includes excavation machinery and truck back-up beepers, and will not exceed the municipal noise bylaws.

### Work Hours

- Monday to Friday from 7:00 a.m. to 7:00 p.m.
- Occasional Saturday work may be required and hours will fall within each municipality's bylaws.
- Night work may be done at busy intersections to limit impacts to traffic.

### Traffic Impacts

- There will be single lane alternating traffic in the work zones controlled by flaggers.
- Two-way traffic will be maintained at busy intersections during rush hour.
- There will be temporary parking impacts when work is being completed. Parking signs will be posted in advance.

### Access

- Access to residents and businesses will be temporarily impacted when work is underway and will be reinstated at the end of each work day. Residents will be notified of temporary closures in advance.

Construction of the Residual Solids Conveyance Line is anticipated to be complete in spring 2020.

*Thank you for your patience as this work is completed.*

(Continued on next page)

---

**Any questions about the work, please contact the Project Team.**



**24/7 Phone Line**  
1.844.815.6132




**Email**  
[wastewater@crd.bc.ca](mailto:wastewater@crd.bc.ca)



**Website**  
[wastewaterproject.ca](http://wastewaterproject.ca)

**Construction Progress Map**

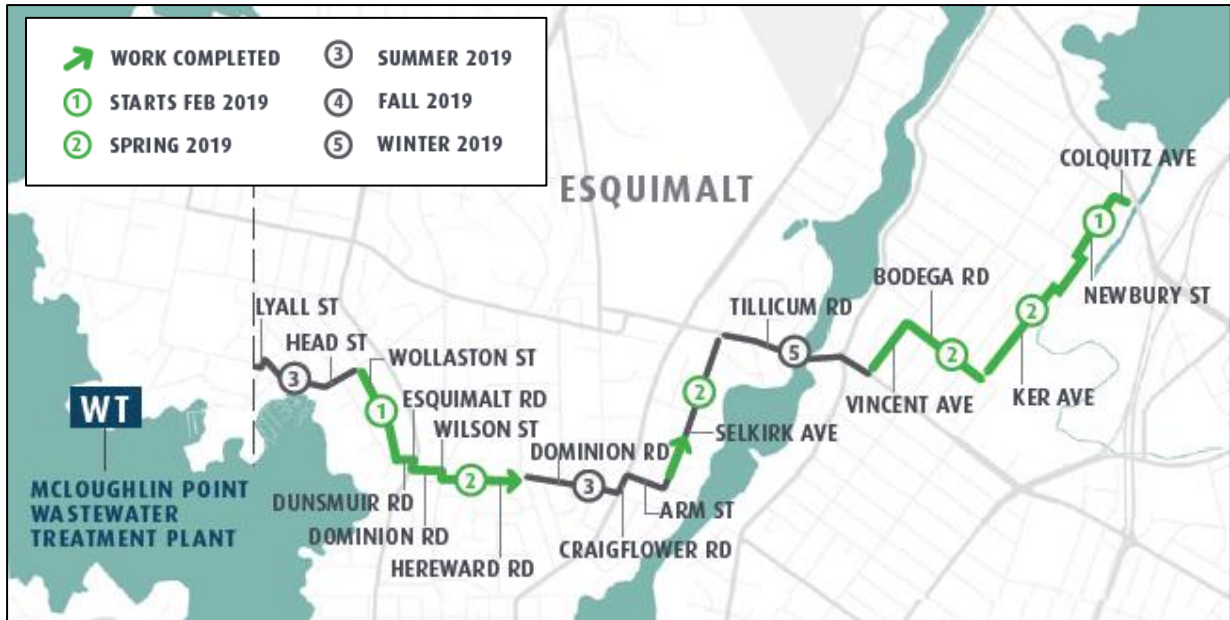

Progress as of May 10, 2019

Construction schedule is subject to change. Please check our website for weekly updates to progress map.

**Any questions about the work, please contact the Project Team.**



**24/7 Phone Line**  
1.844.815.6132



**Email**  
wastewater@crd.bc.ca



**Website**  
wastewaterproject.ca
